Project Planning Phase

Project Planning Template (Product Backlog, Sprint Planning, Stories, Story points)

Date	22 September 2026
Team ID	
Project Name	An Employee Requests Installation of Licensed Software through the Service Catalog
Maximum Marks	5 Marks

Product Backlog, Sprint Schedule, and Estimation

Sprint	Functional Requirement (Epic)	User Story Number	User Story / Task	Story Points	Priority
Sprint-1	Software Catalog Management	USN-1	As an employee, I can view the available licensed software in the Service Catalog so that I can select the software required for my work.	3	High
Sprint-1	Software Catalog Management	USN-2	As an employee, I can select the required licensed software from the Service Catalog.	2	High
Sprint-1	Software Request Submission	USN-3	As an employee, I can provide software, employee, device, and business justification details while submitting a request.	2	High
Sprint-1	Software Request Submission	USN-4	As an employee, I can submit a software installation request through the Service Catalog.	3	High

Sprint-1	Request Validation	USN-5	As a system, I can validate the mandatory fields before allowing the employee to submit the request.	2	High
Sprint-1	Request Validation	USN-6	As a system, I can generate a unique request/RITM number after successful submission.	1	Medium
Sprint-1	Request Tracking	USN-7	As an employee, I can view the current status of my software installation request.	2	Medium
Sprint-2	Approval Management	USN-8	As a manager, I can review the employee's software request and verify the business justification.	3	High
Sprint-2	Approval Management	USN-9	As a manager, I can approve or reject the software request with comments.	2	High
Sprint-2	Workflow Automation	USN-10	As a system, I can automatically route the submitted request to the appropriate manager for approval.	5	High
Sprint-2	IT Fulfillment	USN-11	As an IT support member, I can receive approved software requests assigned to my group.	2	High
Sprint-2	License Management	USN-12	As an IT support member, I can verify the availability of the requested software	3	High

			license before installation.		
Sprint-2	IT Fulfillment	USN-13	As an IT support member, I can create and manage a fulfillment task for software installation.	3	High
Sprint-2	IT Fulfillment	USN-14	As an IT support member, I can update the request status after installing the software.	2	Medium
Sprint-3	Notifications	USN-15	As an employee, I can receive a notification when my software request is submitted successfully.	2	Medium
Sprint-3	Notifications	USN-16	As an employee, I can receive notifications when my request is approved or rejected.	2	Medium
Sprint-3	Notifications	USN-17	As an employee, I can receive a notification when the software installation is completed.	2	Medium
Sprint-3	Request Closure	USN-18	As an IT support member, I can close the request after successful software installation.	2	High
Sprint-3	Reporting	USN-19	As an administrator, I can view reports of software requests based on status and software type.	3	Medium

Sprint-3	Request History	USN-20	As an administrator, I can view the complete history of software requests, approvals, and fulfillment activities.	2	Medium
Sprint-3	Security & Access Control	USN-21	As an administrator, I can control access to software requests based on user roles and responsibilities.	3	High

Project Tracker, Velocity & Burndown Chart

Sprint	Total Story Points	Duration	Sprint Start Date	Sprint End Date (Planned)	Story Points Completed (as on Planned End Date)	Sprint Release Date (Actual)
Sprint-1	**15**	**6 Days**	**05 Oct 2026**	**10 Oct 2026**	**15**	**10 Oct 2026**
Sprint-2	**20**	**6 Days**	**12 Oct 2026**	**17 Oct 2026**	**20**	**17 Oct 2026**
Sprint-3	**16**	**6 Days**	**19 Oct 2026**	**24 Oct 2026**	**16**	**24 Oct 2026**

Formula

Velocity = Total Story Points Completed / Number of Sprints

Total Story Points:

15 + 20 + 16 = 51

Number of Sprints:

3

Therefore,

Velocity = 51 / 3

Average Velocity = 17 Story Points per Sprint

So, the team's average velocity is 17 Story Points per Sprint.

Average Velocity per Day

Since each sprint has 6 days:

Average Velocity per Day = 17 / 6

≈ 2.83 Story Points per Day

Burndown Chart:

servicenow

An Employee Requests Installation of Licensed Software through the Service Catalog

Sprint Burndown Chart – Project Tracking & Progress

Agile Project Management
Track | Monitor | Deliver

About the Report

The Sprint Burndown Chart helps us track the progress of the current sprint by showing the remaining and completed story points over time.


It gives a clear view of whether the team is on track to complete the planned work within the sprint duration.

Key Insights

- Shows daily progress of story points.
- Helps identify delays or roadblocks in the sprint.
- Improves team focus and productivity.
- Ensures timely delivery of features and fixes.

Sprint Details (Example)

Sprint	: Sprint 1
Duration	: 6 Days
Start Date	: 05 Oct 2026
End Date (Planned)	: 10 Oct 2026
Story Points (Planned)	: 15
Story Points (Completed)	: 15
Sprint Status	: Completed

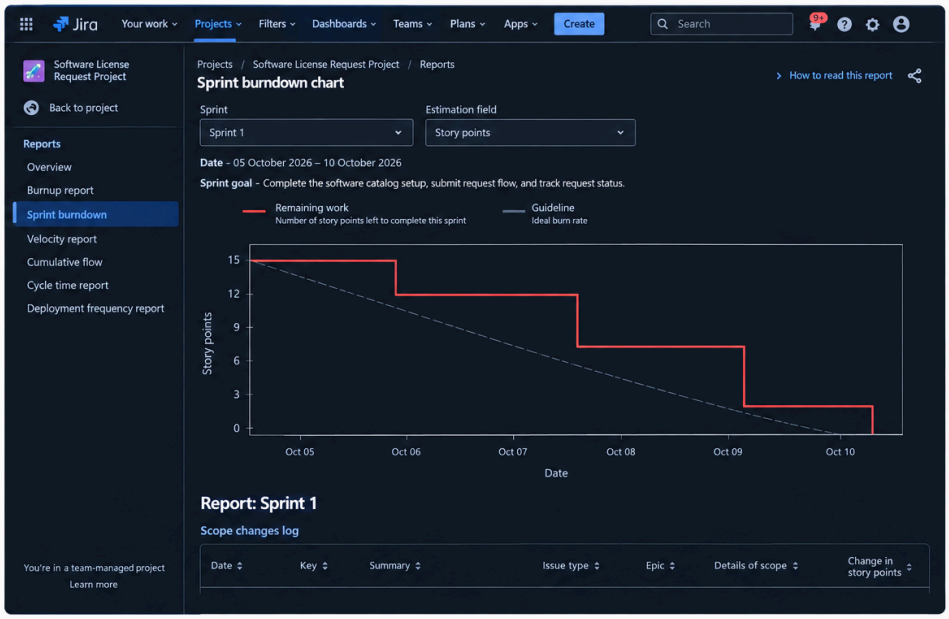

Conclusion

The burndown chart shows steady progress in Sprint 1, with all 15 story points completed by the end of the sprint.
This indicates that the team is on track and the sprint goal has been successfully achieved.
